RECORD OF SURVEY

SHOWING THE CENTERLINE OF THE SAN BERNARDINO VALLEY MUNICIPAL WATER DISTRICT PIPELINE

LUDWIG ENGINEERING

JANUARY 1976

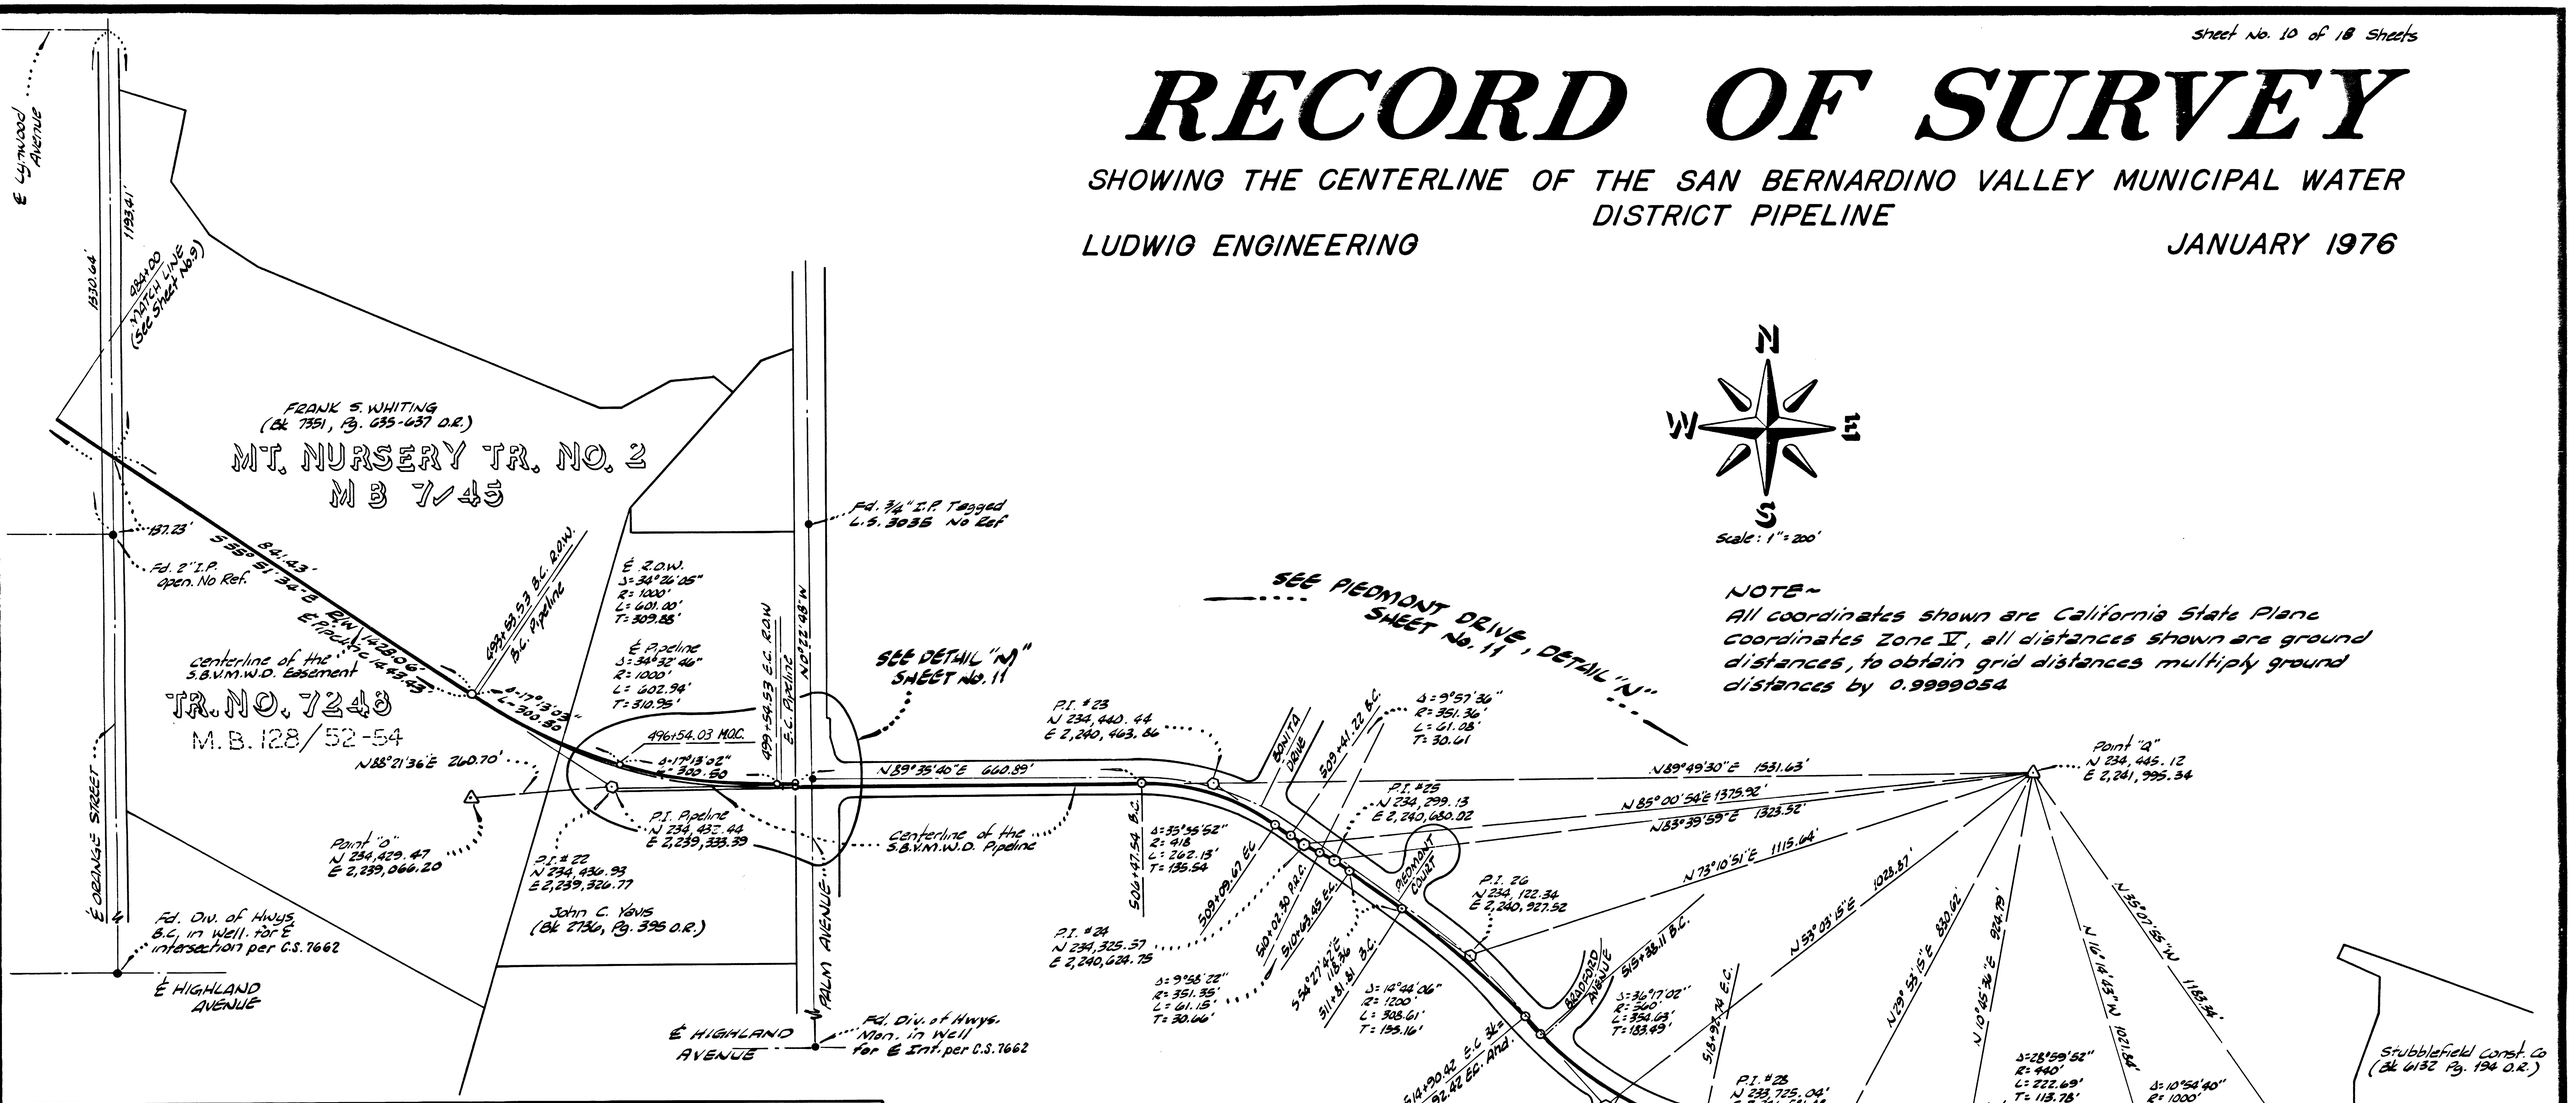

CENTERLINE P.I. TIES

P.I. NO.	BEARING	DISTANCE	DESCRIPTION
19	West	116.23'	Nail in top of Block Wall
	S.W.	120.22'	Nail & Flasher S.W. side Power Pole No. 1407468 E
	N.W.	100.00'	Nail in curb
20	S.W	46.95'	Chis "X" top of fire hydrant
	S.E.	65.23'	Chis "X" in top of curb
21	N.W.	60.40'	Nail in S.W. side of Power Pole No. 58/561 H
	S.W.	60.80'	Screw in top of curb at the end of curb
22	North	146.24'	Nail in top of conc. Flume
	N.E	133.28'	Nail in N.W. side of Avocado Tree
23	N.W.	14.41'	Nail in curb
	S.W.	35.37'	Nail in curb
	N.E.	73.50'	Nail at M.O.C. of curb return
24	N.E.	39.76'	Nail in curb
	S.W.	70.03'	Nail in curb
	S.E.	16.57'	Nail in curb
25	N.E.	30.61'	Nail in curb
	S.W.	47.15'	Nail in curb
	S.E.	36.71'	Nail in curb
26	N.W.	43.61'	Nail in curb
	S.W.	38.95'	Nail in curb
	S.E.	61.25'	Nail in curb
27	N.W.	16.40'	Nail in curb at M.O.C., S.W. Curb Return
	N.E.	57.89'	Nail in curb
	East	40.23'	Nail in curb at M.O.C., S.E. Curb Return

CENTERLINE P.I. TIES

P.I. NO.	BEARING	DISTANCE	DESCRIPTION
28	N.W.	40.01'	Nail in Curb
	S.W.	34.99'	Nail in Curb
	N.E.	22.06'	Nail in Curb
29	North	32.69'	Nail in Curb
	S.W.	42.59'	Nail in Curb
	S.E.	36.69'	Nail in Curb
30	N.E.	38.56	Nail in Curb
	S.E.	41.70'	Nail in Curb
	S.W.	73.60'	Nail in Curb at M.O.C. of S.E. Curb return
31	N.W.	78.15	Nail in Curb
	S.W.	80.15	Nail in Curb
	North	6.23	Nail in Curb
