RECORD OF SURVEY

SHOWING THE CENTERLINE OF THE SAN BERNARDINO VALLEY MUNICIPAL WATER DISTRICT PIPELINE

LUDWIG ENGINEERING

JANUARY 1976

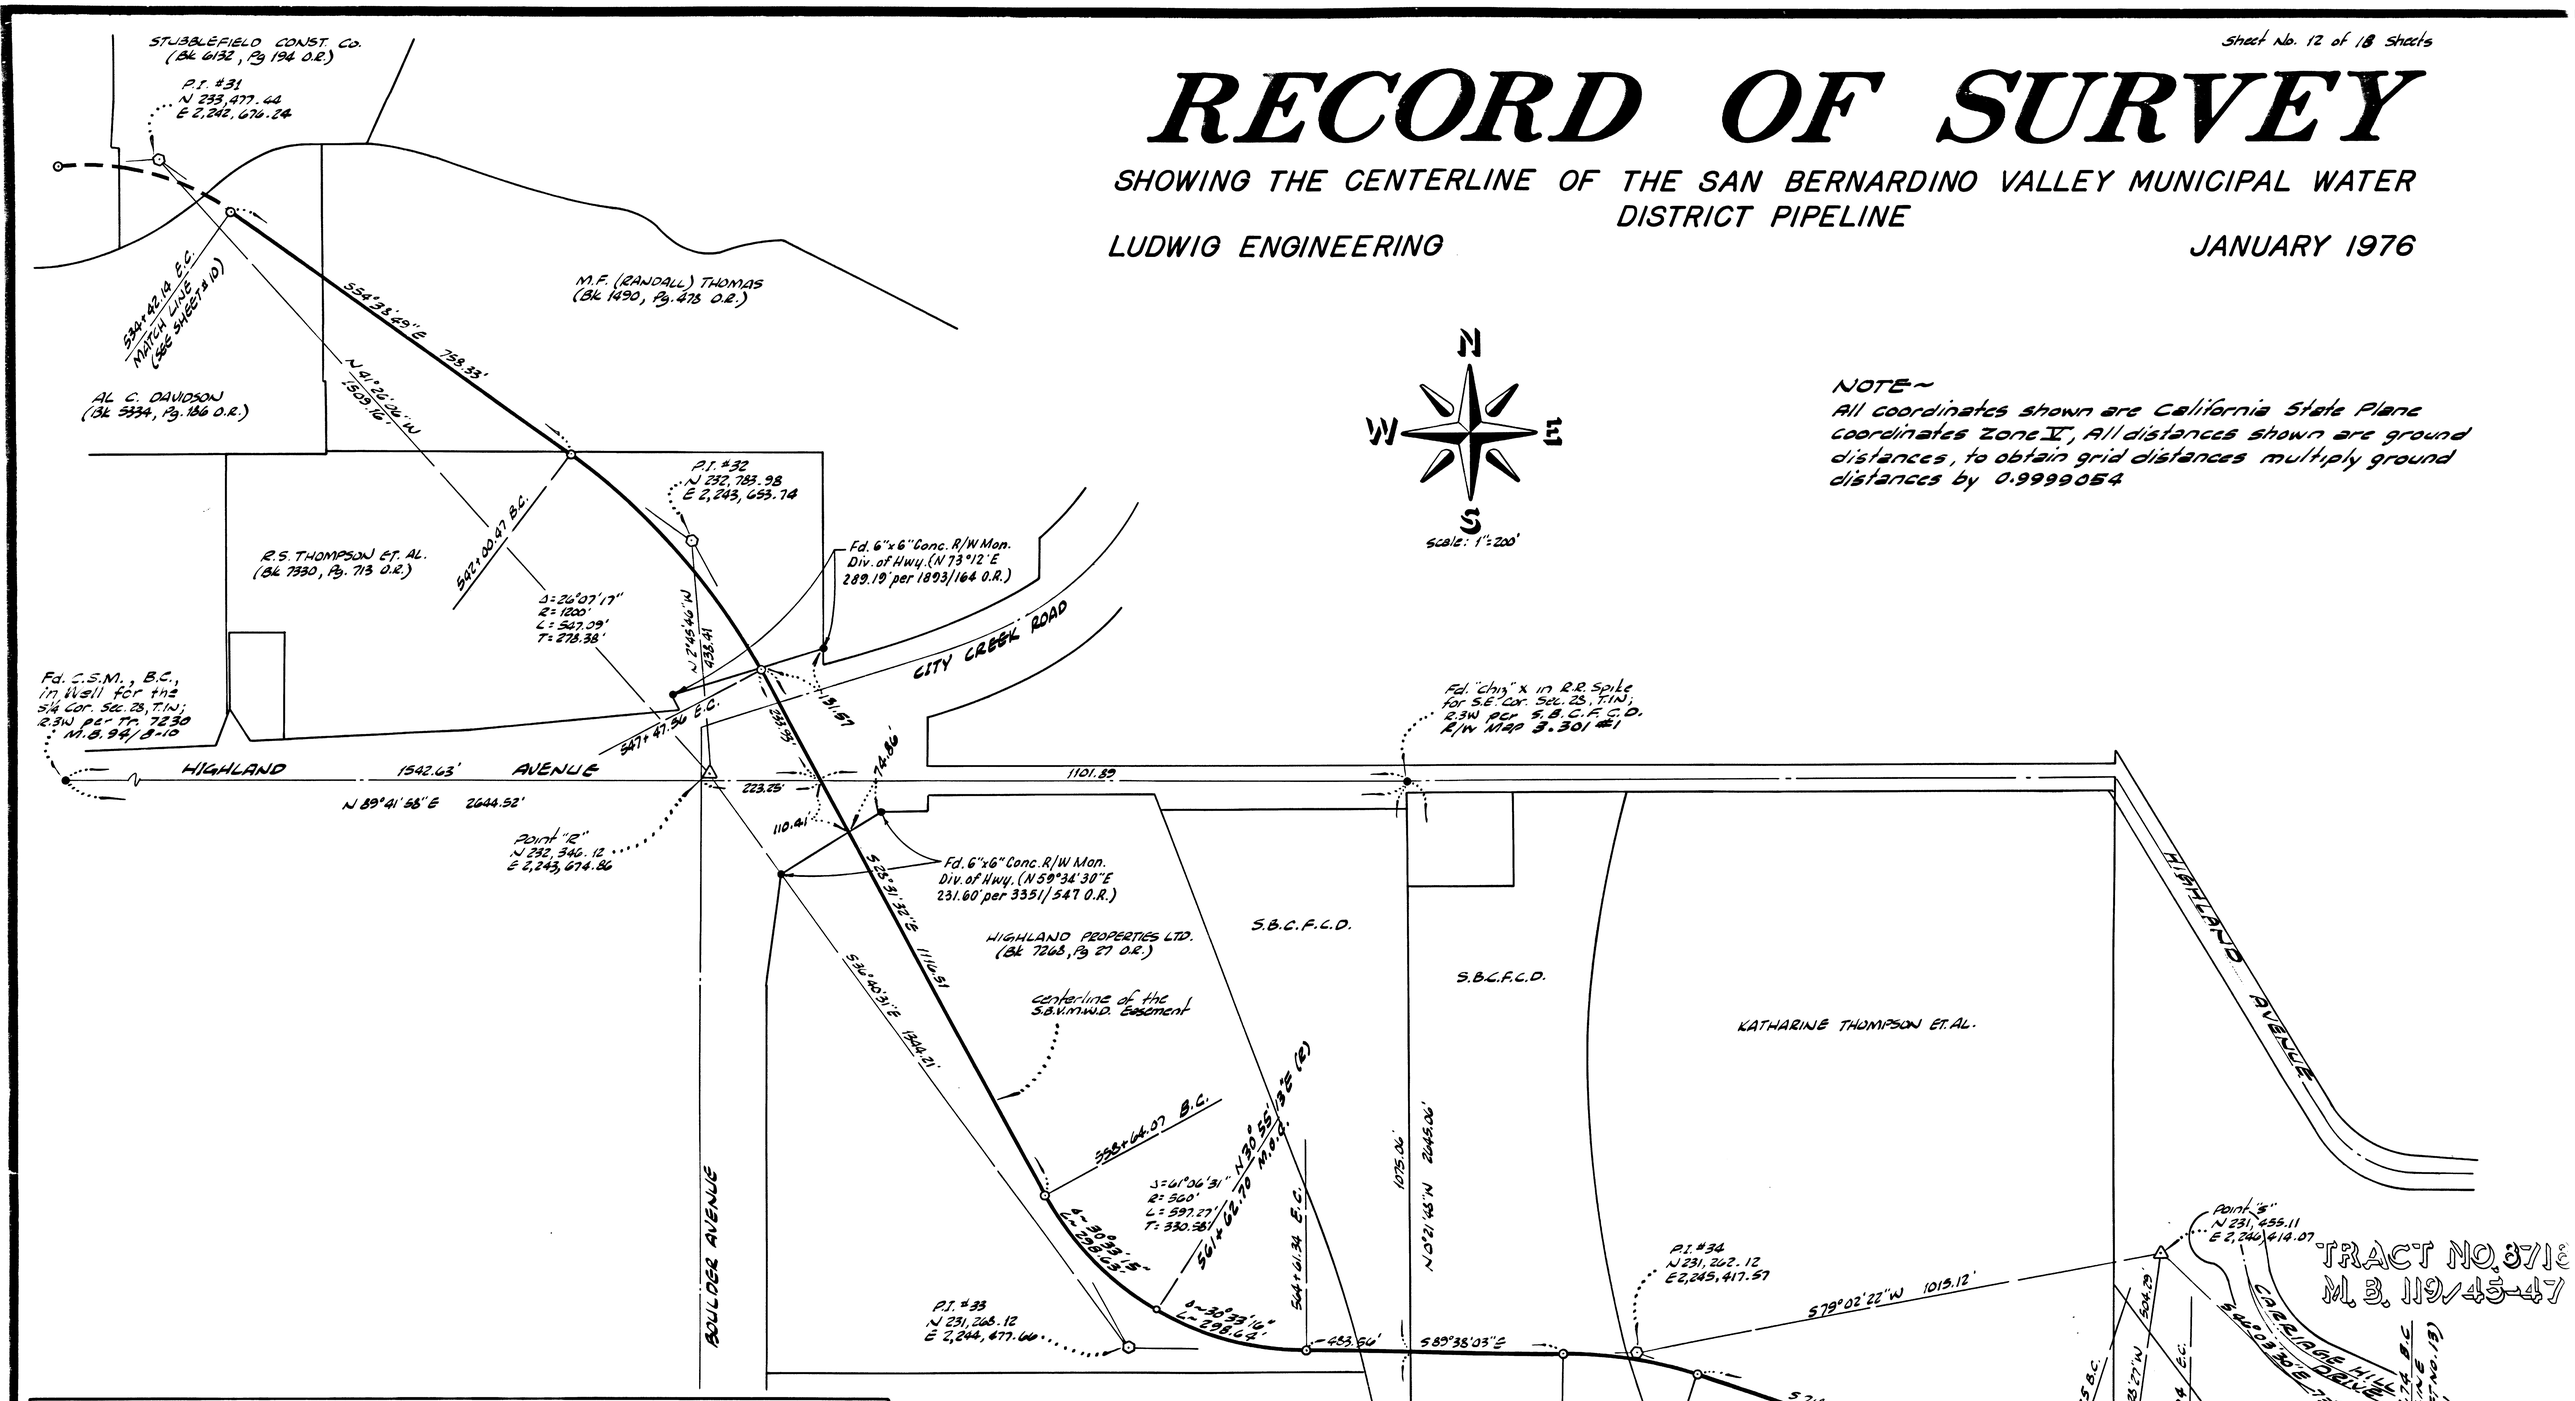

NOTE~
All coordinates shown are California State Plane coordinates Zone V, All distances shown are ground distances, to obtain grid distances multiply ground distances by 0.9999054

CENTERLINE P.I. TIES

P.I. No.	BEARING	DISTANCE	DESCRIPTION
32	East	23.60'	Nail in north side of Orange Tree
	North	39.32'	Nail in east side of Orange Tree
33	N.E.	14.65'	Nail in orange tree
	South	42.99	Nail in West side of Power Pole No. 256541 E
	S.E.	114.36'	Chis. "X" in top of fence post near building
34	S.W.	19.97'	Chis. "X" in top of concrete manhole structure (north side)
	S.W.	21.14'	Chis. "X" in top of concrete manhole structure (south side)
	S.E.	95.24'	N.E. corner of City Creek turnout structure, 5' below top
35	N.W	87.74'	Nail in orange tree
	North	66.59'	Nail & tag in flume
	N.E.	6.52'	Chis. "X" in top of southerly conc. manhole structure (North side)
	S.E.	4.09'	Chis. "X" in top of southerly concrete manhole structure (South side)
