RECORD OF SURVEY

SHOWING THE CENTERLINE OF THE SAN BERNARDINO VALLEY MUNICIPAL WATER DISTRICT PIPELINE

LUDWIG ENGINEERING

JANUARY 1976

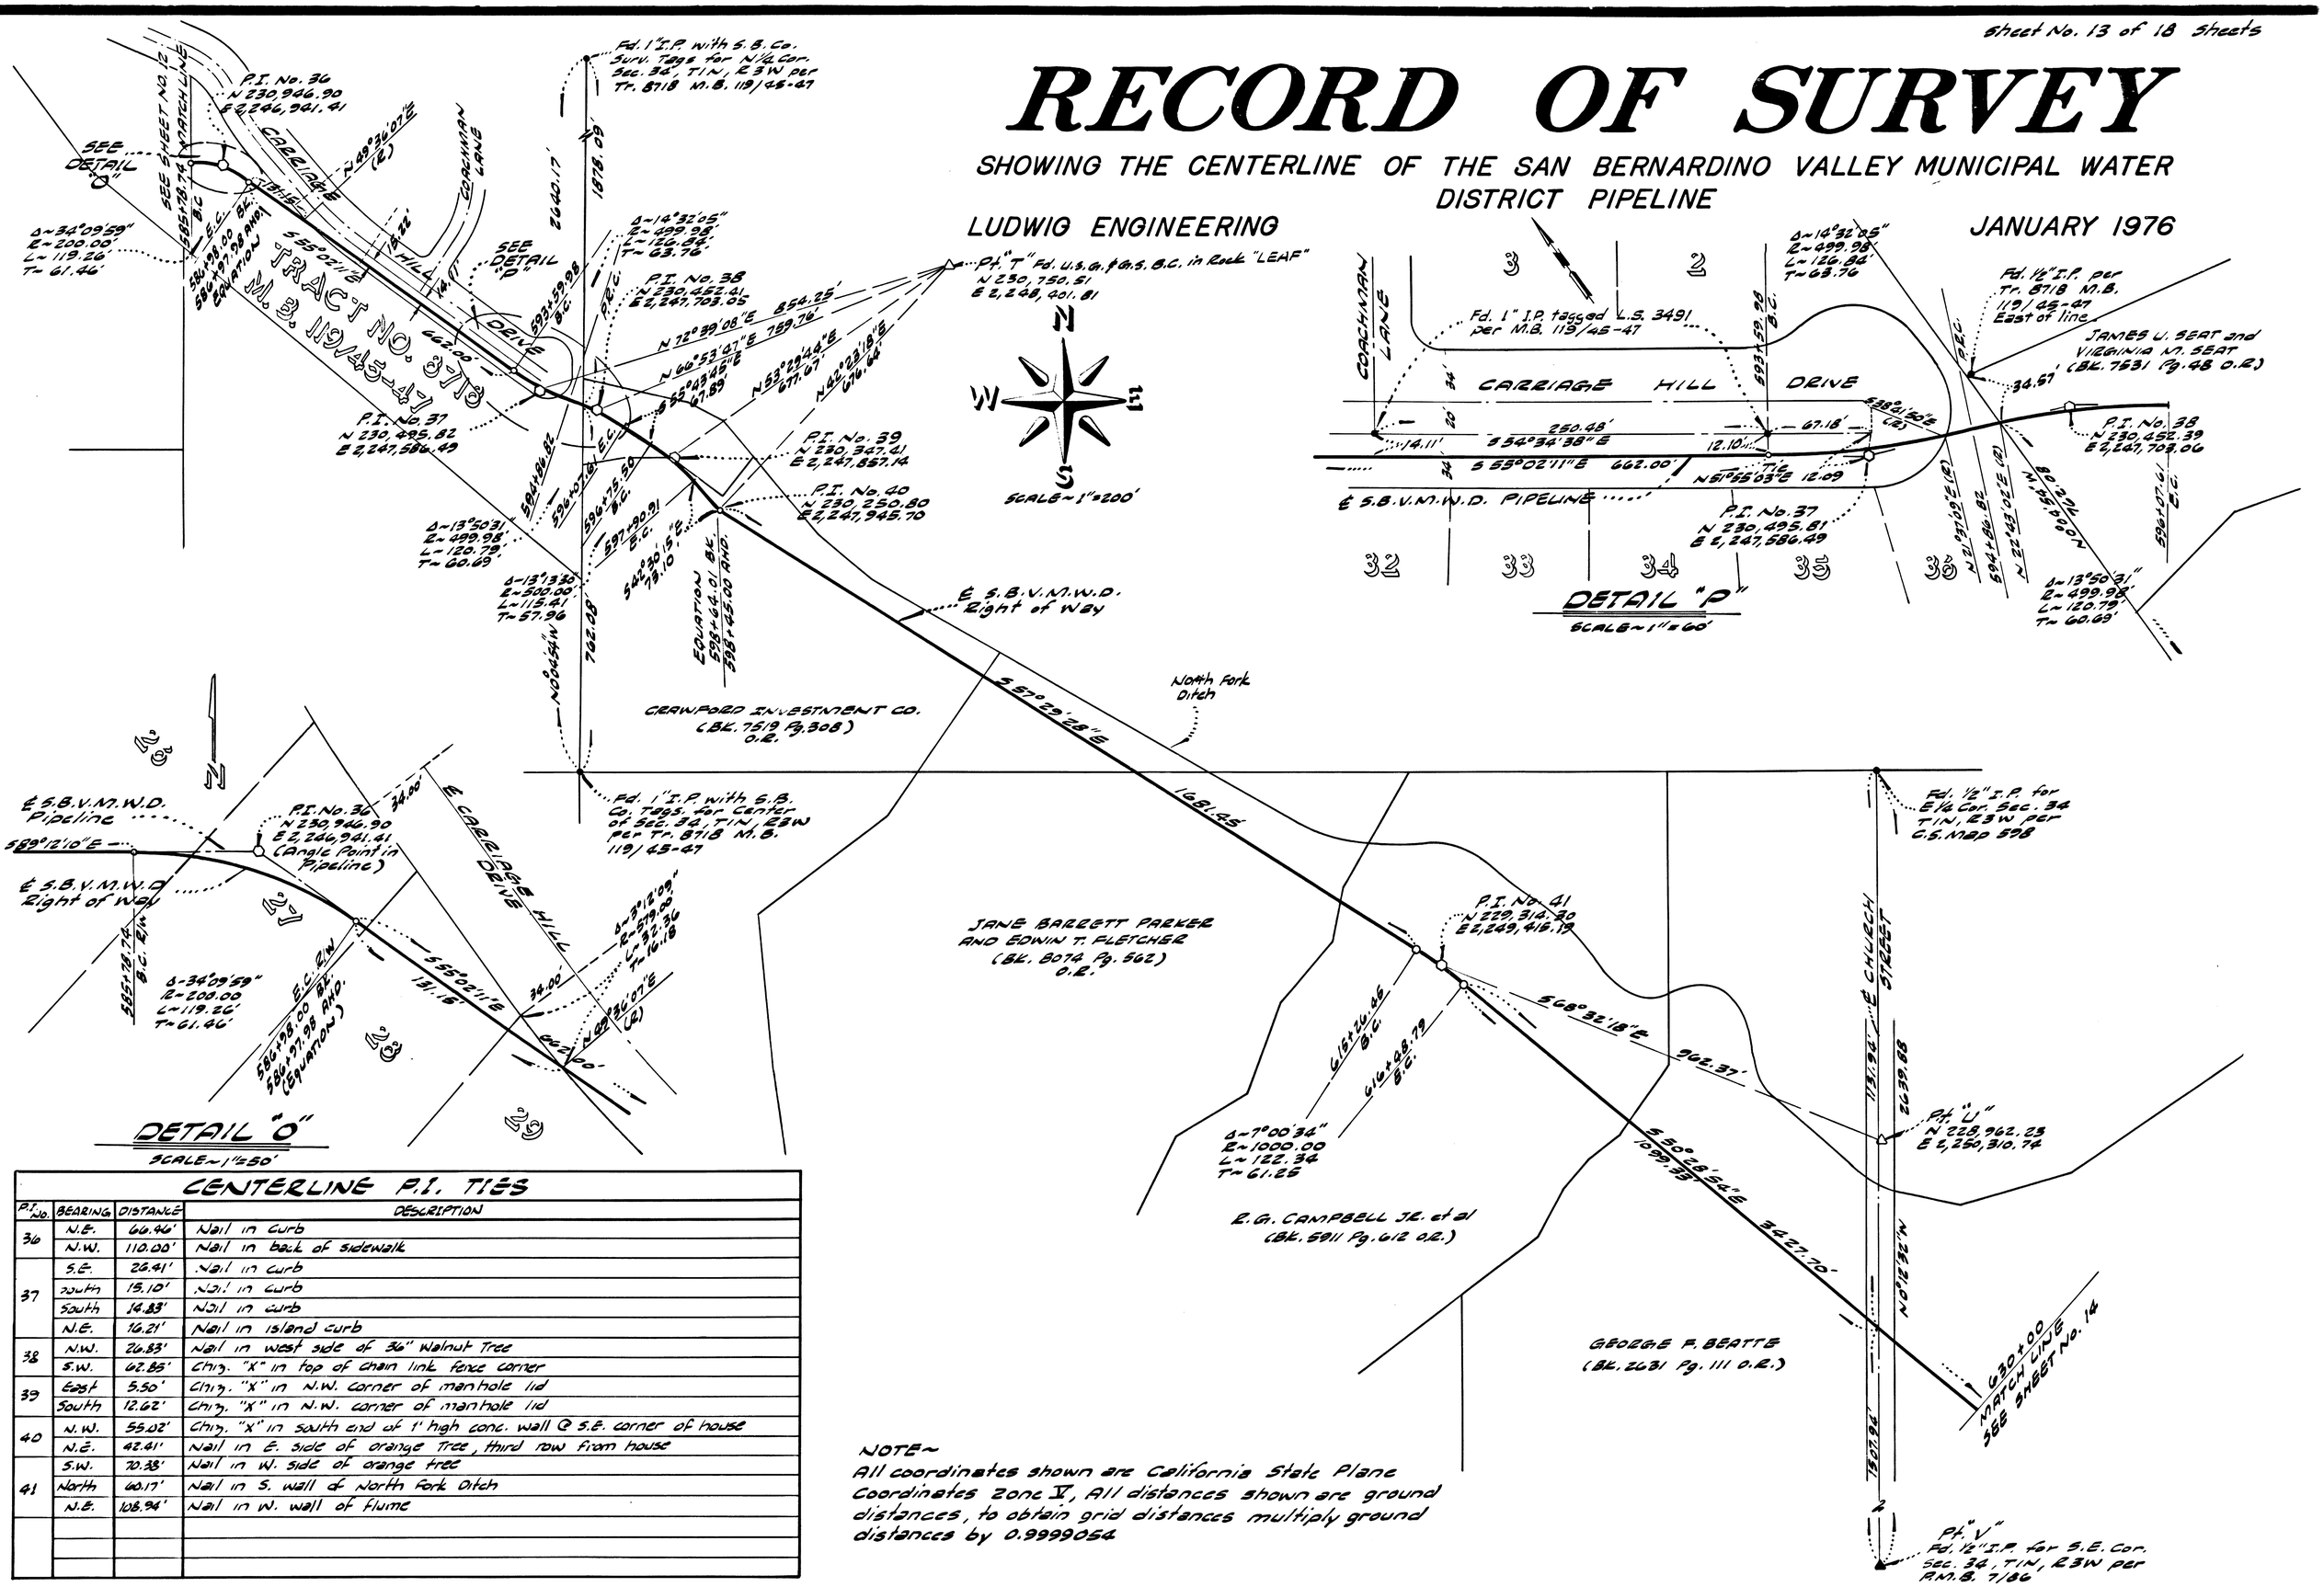

CENTERLINE P.I. TIES			
P.I. No.	BEARING	DISTANCE	DESCRIPTION
36	N.E.	66.46'	Nail in curb
	N.W.	110.00'	Nail in back of sidewalk
37	S.E.	26.41'	Nail in curb
	South	15.10'	Nail in curb
	South	14.83'	Nail in curb
	N.E.	16.21'	Nail in island curb
38	N.W.	26.83'	Nail in west side of 36" Walnut Tree
	S.W.	62.85'	Chiz. "X" in top of chain link fence corner
39	East	5.50'	Chiz. "X" in N.W. corner of manhole lid
	South	12.62'	Chiz. "X" in N.W. corner of manhole lid
40	N.W.	55.02'	Chiz. "X" in south end of 1' high conc. wall @ S.E. corner of house
	N.E.	42.41'	Nail in E. side of orange tree, third row from house
41	S.W.	70.38'	Nail in W. side of orange tree
	North	60.17'	Nail in S. wall of North Fork Ditch
	N.E.	108.94'	Nail in W. wall of flume

NOTE~
All coordinates shown are California State Plane Coordinates Zone V, All distances shown are ground distances, to obtain grid distances multiply ground distances by 0.9999054
